
ONE BUILDING ON THE MAP. THIRTY-EIGHT ON THE CAMPUS.

TAFE NSW Richmond: each building drawn in Plotlay over NSW aerial imagery, coloured by where its outline came from.

Buildings by outline source: blue traced from the Microsoft footprint, gold traced (not in the footprints), red the Microsoft footprint as it is

- Traced over NSW Imagery, started from the Microsoft footprint and fitted to the roof edges
- Traced over NSW Imagery (not in the Microsoft footprints)
- Microsoft footprint, picked as it is (a complex roof, not refined)

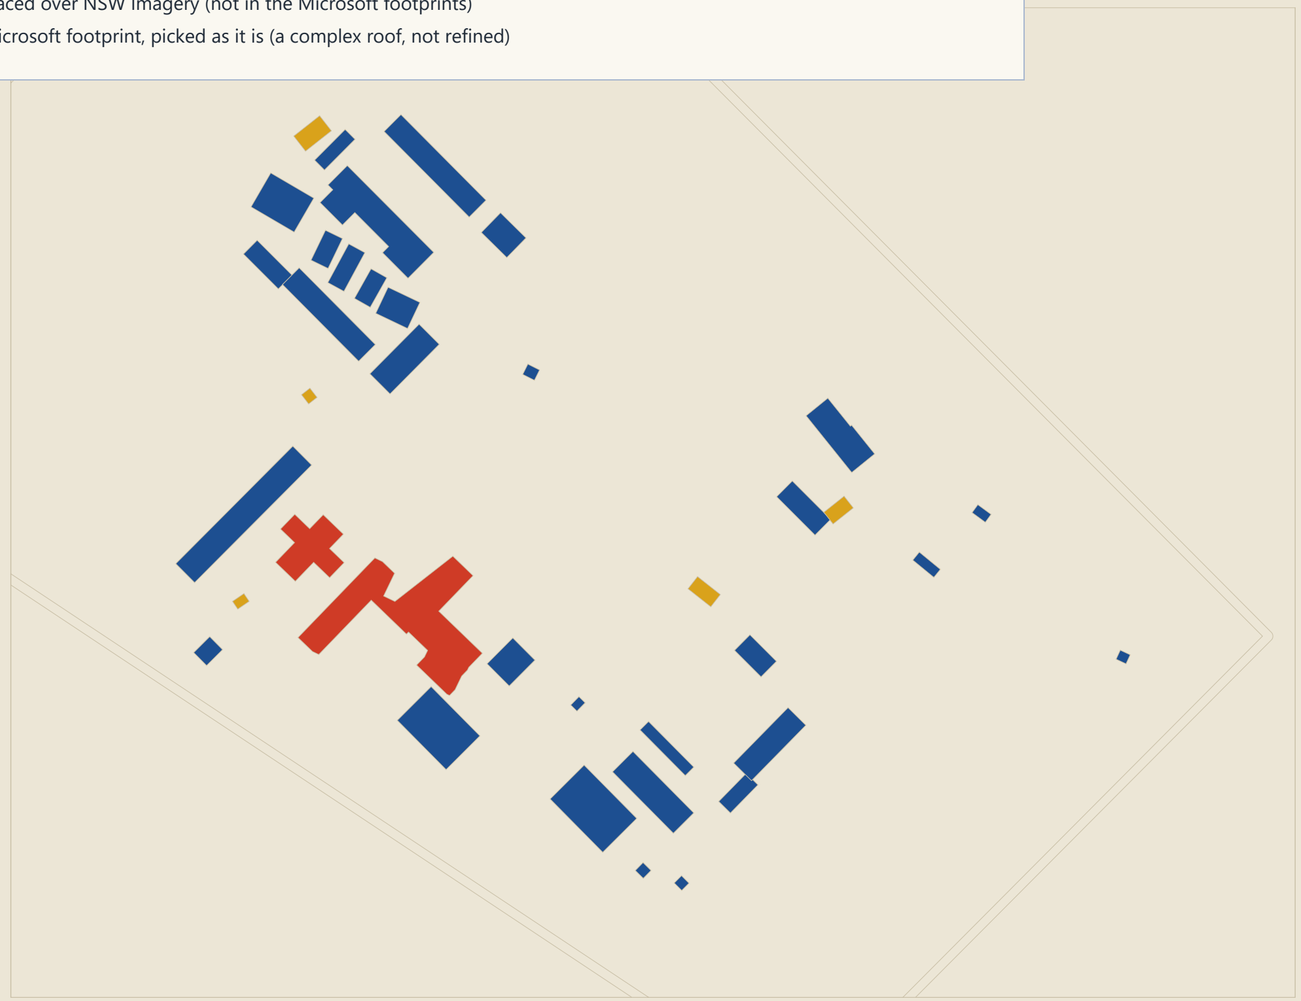

Buildings	In no open data	Microsoft offset, median m
38	5	2.23

Each building


Building	Outline from	Accuracy (m)	Footprint (m^2)	Microsoft offset (m)
B01	Traced over NSW Imagery (not in the Microsoft f...	0.5	200	
B02	Traced over NSW Imagery, started from the Micr...	0.5	192	2.83
B03	Traced over NSW Imagery, started from the Micr...	0.5	624	1.67
B04	Traced over NSW Imagery, started from the Micr...	0.5	1,362	2.21
B05	Traced over NSW Imagery, started from the Micr...	0.5	914	2.44
B06	Traced over NSW Imagery, started from the Micr...	0.5	313	1.88
B07	Traced over NSW Imagery, started from the Micr...	0.5	305	2.24
B08	Traced over NSW Imagery, started from the Micr...	0.5	200	2.14
B09	Traced over NSW Imagery, started from the Micr...	0.5	812	2.16
B10	Traced over NSW Imagery, started from the Micr...	0.5	257	2.00
B11	Traced over NSW Imagery, started from the Micr...	0.5	196	2.02
B12	Traced over NSW Imagery, started from the Micr...	0.5	324	2.32
B13	Traced over NSW Imagery (not in the Microsoft f...	0.5	39	
B14	Traced over NSW Imagery, started from the Micr...	0.5	634	3.13
B15	Traced over NSW Imagery, started from the Micr...	0.5	48	2.43
B16	Traced over NSW Imagery, started from the Micr...	0.5	667	1.50
B17	Traced over NSW Imagery, started from the Micr...	0.5	1,410	4.84
B18	Microsoft footprint, picked as it is (a complex roo...	2.5	866	
B19	Traced over NSW Imagery, started from the Micr...	0.5	384	2.17
B20	Traced over NSW Imagery (not in the Microsoft f...	0.5	122	
B21	Traced over NSW Imagery, started from the Micr...	0.5	51	2.29
B22	Traced over NSW Imagery (not in the Microsoft f...	0.5	41	
B23	Microsoft footprint, picked as it is (a complex roo...	2.5	2,957	
B24	Traced over NSW Imagery (not in the Microsoft f...	0.5	143	
B25	Traced over NSW Imagery, started from the Micr...	0.5	89	2.13
B26	Traced over NSW Imagery, started from the Micr...	0.5	132	0.90
B27	Traced over NSW Imagery, started from the Micr...	0.5	364	1.66
B28	Traced over NSW Imagery, started from the Micr...	0.5	32	2.16
B29	Traced over NSW Imagery, started from the Micr...	0.5	261	3.29
B30	Traced over NSW Imagery, started from the Micr...	0.5	35	2.45
B31	Traced over NSW Imagery, started from the Micr...	0.5	1,055	1.48

Aerial imagery, and the outlines drawn over it: (c) State of New South Wales (Spatial Services), CC BY 3.0 AU. Two outlines from Microsoft Global ML Building Footprints, CDLA Permissive 2.0. Map context: NSW Cadastre lots (Spatial Services, CC BY 3.0 AU), ABS ASGS 2021 suburbs (CC BY 4.0). Shapes made in Plotlay (getplotlay.com). Accuracy depends on the imagery and how each outline was drawn.


WHERE EACH OUTLINE CAME FROM

Buildings and footprint by source, and how far Microsoft footprints were off the roofs.

Buildings by outline source

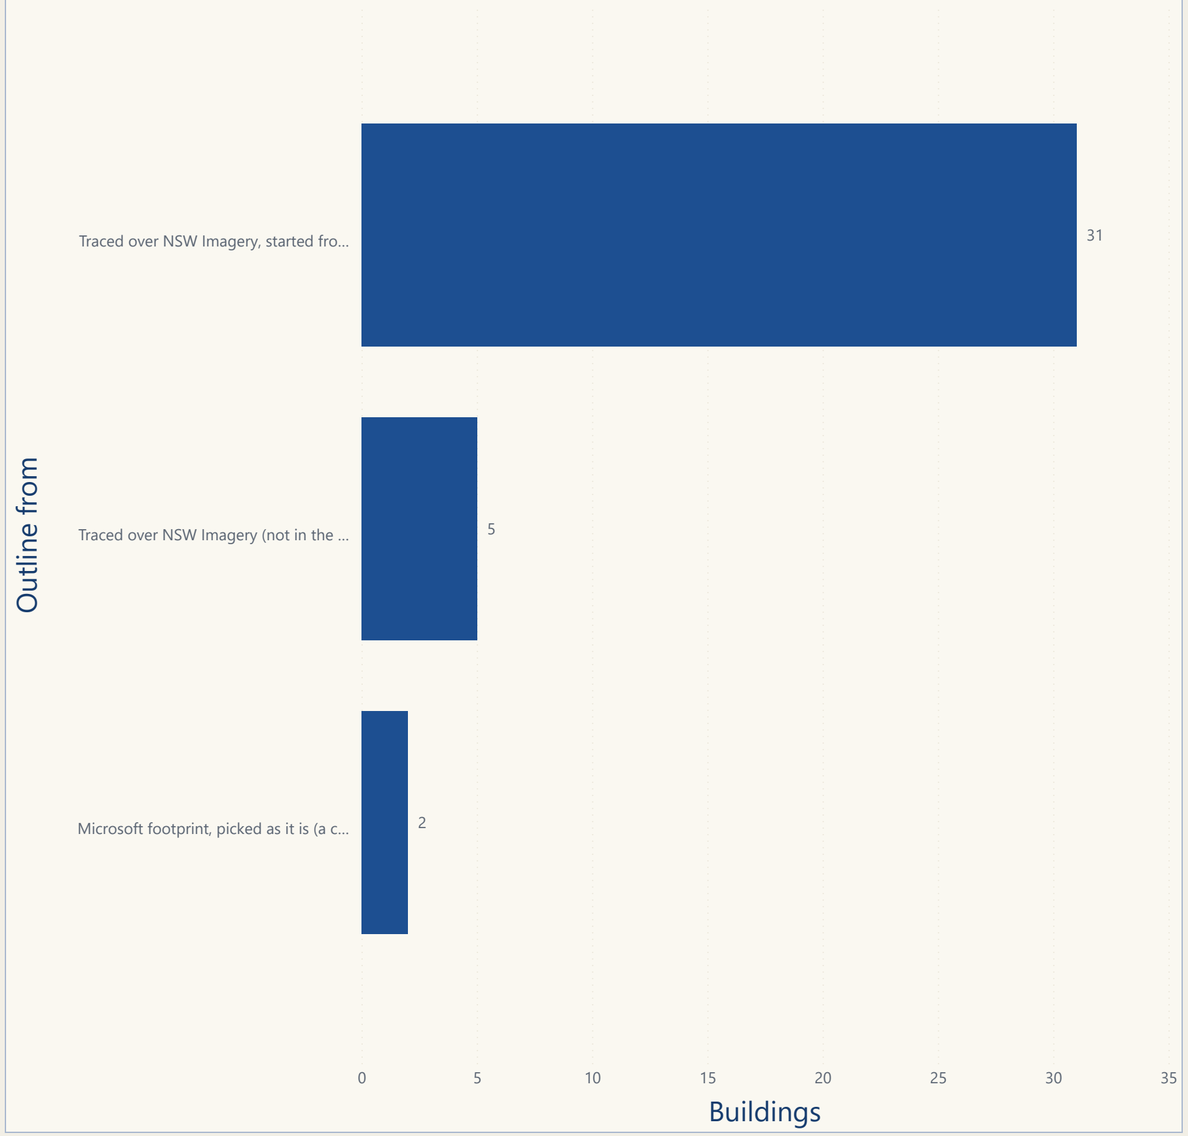

Microsoft offset by building, m (buildings started from a Microsoft footprint)

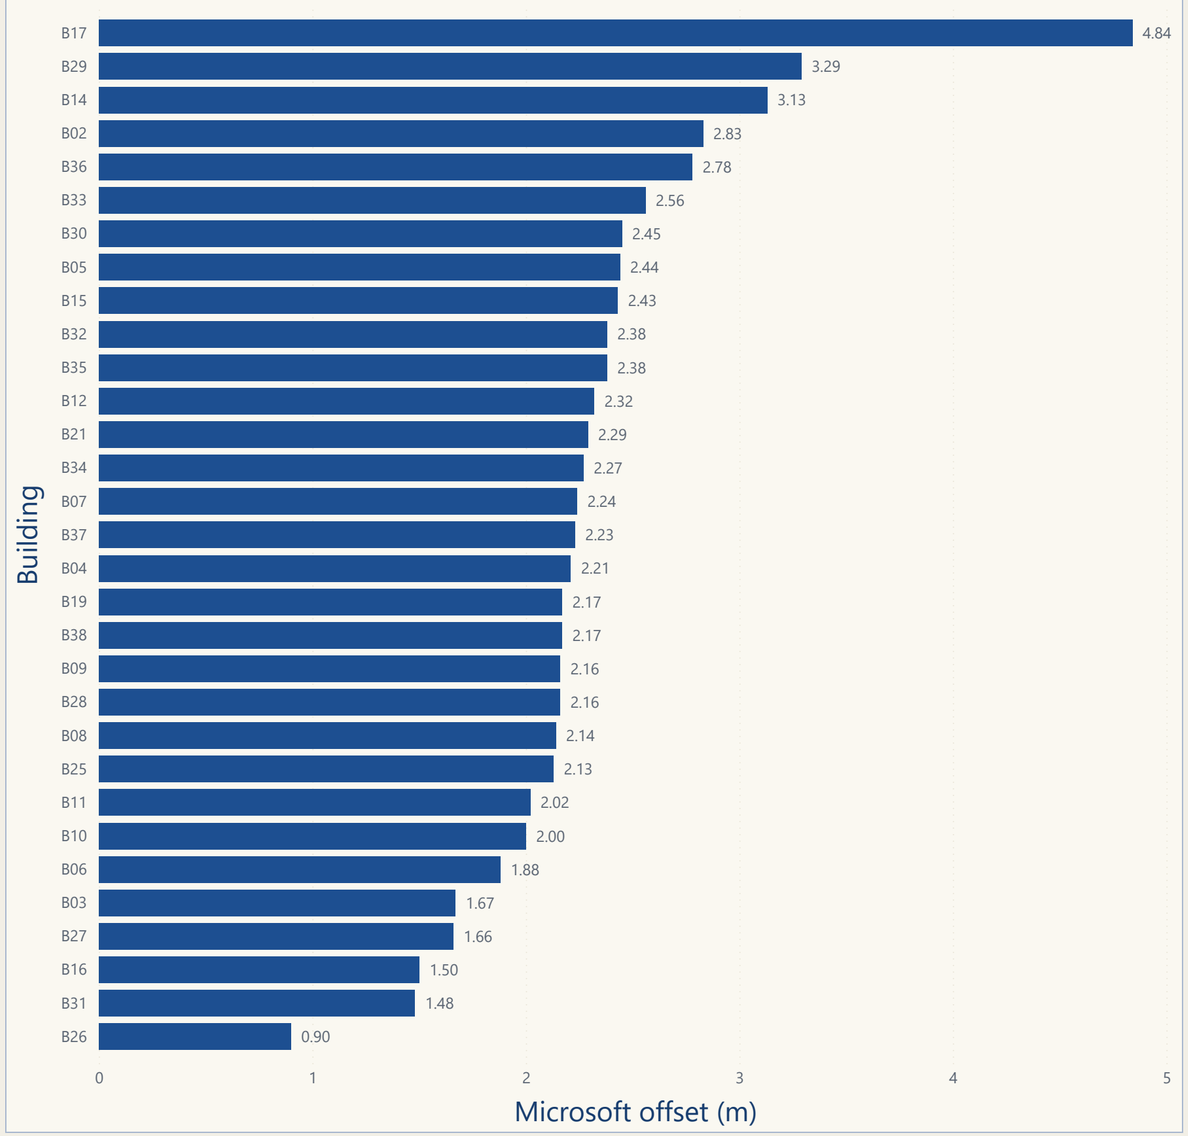

Aerial imagery, and the outlines drawn over it: (c) State of New South Wales (Spatial Services), CC BY 3.0 AU. Two outlines from Microsoft Global ML Building Footprints, CDLA Permissive 2.0. Map context: NSW Cadastre lots (Spatial Services, CC BY 3.0 AU), ABS ASGS 2021 suburbs (CC BY 4.0). Shapes made in Plotlay (getplotlay.com). Accuracy depends on the imagery and how each outline was drawn.

WHERE THE RISK SITS

Every asset in the sample register by likelihood of failure (rows) and consequence (columns), the assets by risk, and each building by its assets at high or extreme risk.

Sample data

Assets (Sample data)

372


High or extreme (Sample data)

70

Past expected life (Sample data)

106

Buildings by assets at high or extreme risk (Sample data)

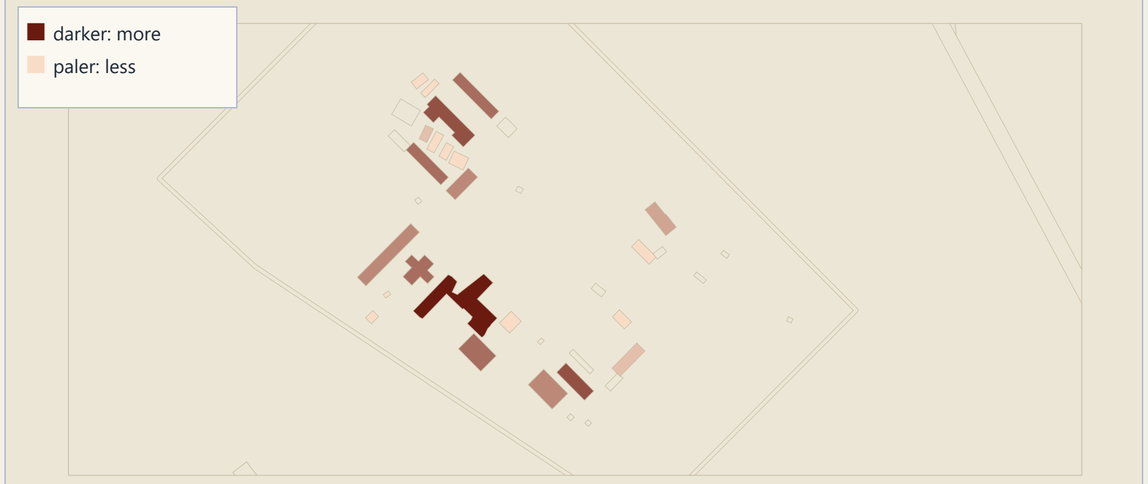

Consequence across the top, 1 minor to 5 severe; likelihood down the side, 1 rare to 5 almost certain.

Risk matrix: assets in each cell (Sample data)

Likelihood	1	2	3	4	5
1	15	42	63	8	1
2	3	13	31	6	2
3	8	24	35	10	1
4	5	38	46	12	
5		8	1		

Assets by risk, highest first (Sample data)

Asset	Asset type	Building	Score	Rating	Drivers
AHU-003	Air handling unit (AHU)	B23	16	High	Past expected life; Poor condition
FD-002	Fire door	B04	16	High	Past expected life; Poor condition; Life safet…
FD-015	Fire door	B32	16	High	Past expected life; Poor condition; Life safet…
FD-016	Fire door	B32	16	High	Past expected life; Poor condition; Life safet…
FD-017	Fire door	B36	16	High	Past expected life; Poor condition; Life safet…
RAP-004	Roof anchor point	B04	16	High	Past expected life; Poor condition
RAP-010	Roof anchor point	B14	16	High	Past expected life; Poor condition
RAP-011	Roof anchor point	B16	16	High	Past expected life; Poor condition
RAP-017	Roof anchor point	B23	16	High	Past expected life; Poor condition
RAP-020	Roof anchor point	B31	16	High	Past expected life; Poor condition
RAP-025	Roof anchor point	B36	16	High	Past expected life; Poor condition
RAP-026	Roof anchor point	B36	16	High	Past expected life; Poor condition
EXL-089	Combination exit and emergency light	B36	15	High	Past expected life; Poor condition; Life safet…
MSB-001	Main switchboard (MSB)	B23	15	High	Poor condition
AHU-002	Air handling unit (AHU)	B17	12	High	Past expected life; Poor condition
DB-005	Distribution board (DB)	B04	12	High	Past expected life; Poor condition
DB-010	Distribution board (DB)	B08	12	High	Past expected life; Poor condition

Sample data: these figures are not about TAFE NSW Richmond or any real building (data/sample/README.md says how they were made). Outlines drawn over NSW Imagery and map lots: (c) State of New South Wales (Spatial Services), CC BY 3.0 AU. Suburbs: ABS ASGS 2021 (CC BY 4.0).

THE WORK ORDER BACKLOG

Open work orders by priority and building, and work orders raised over twelve months, reactive against planned.

Sample data

Open (Sample data)

33


Overdue (Sample data)

9


Raised in 12 months (Sample data)

1,010

Open by priority and building (Sample data)

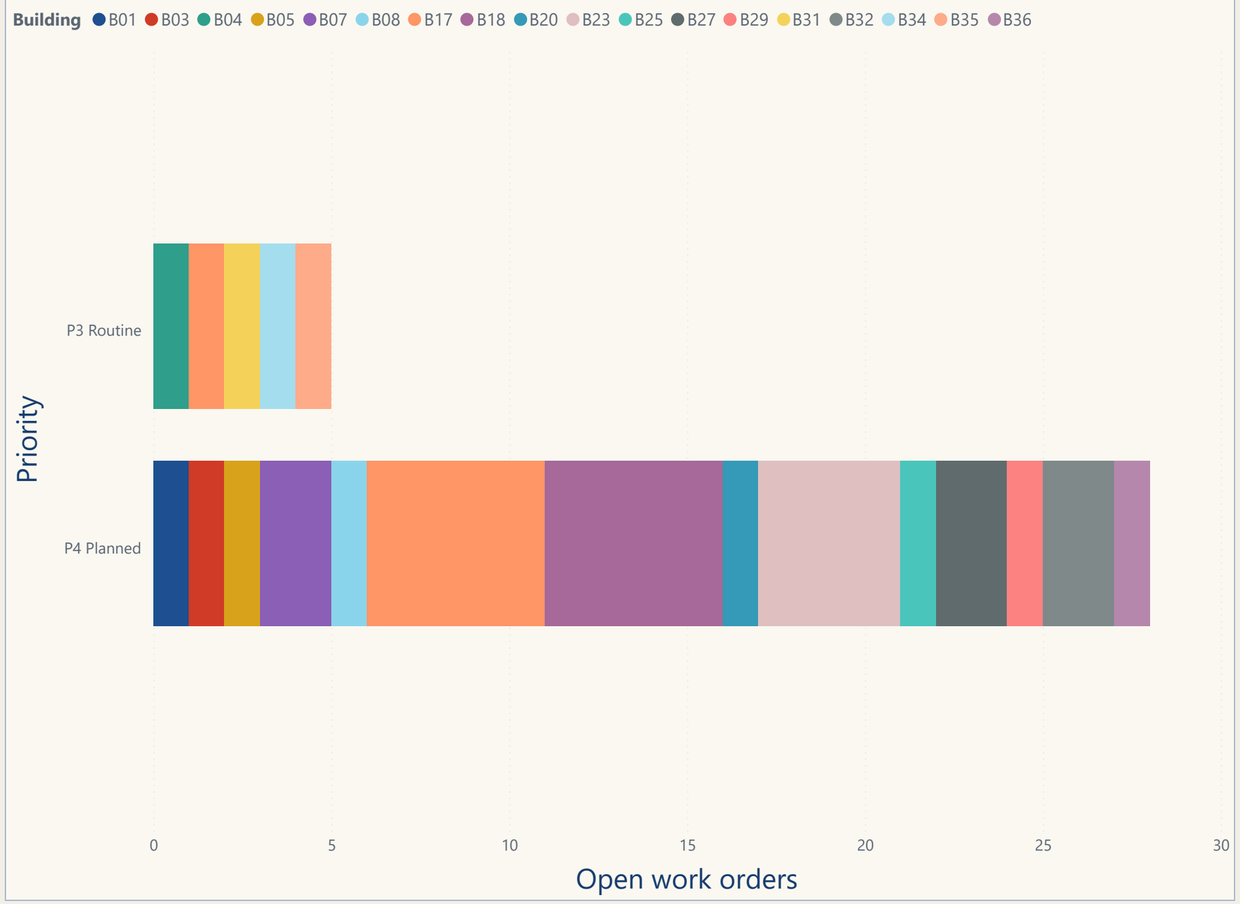

Raised each month, reactive and planned (Sample data)

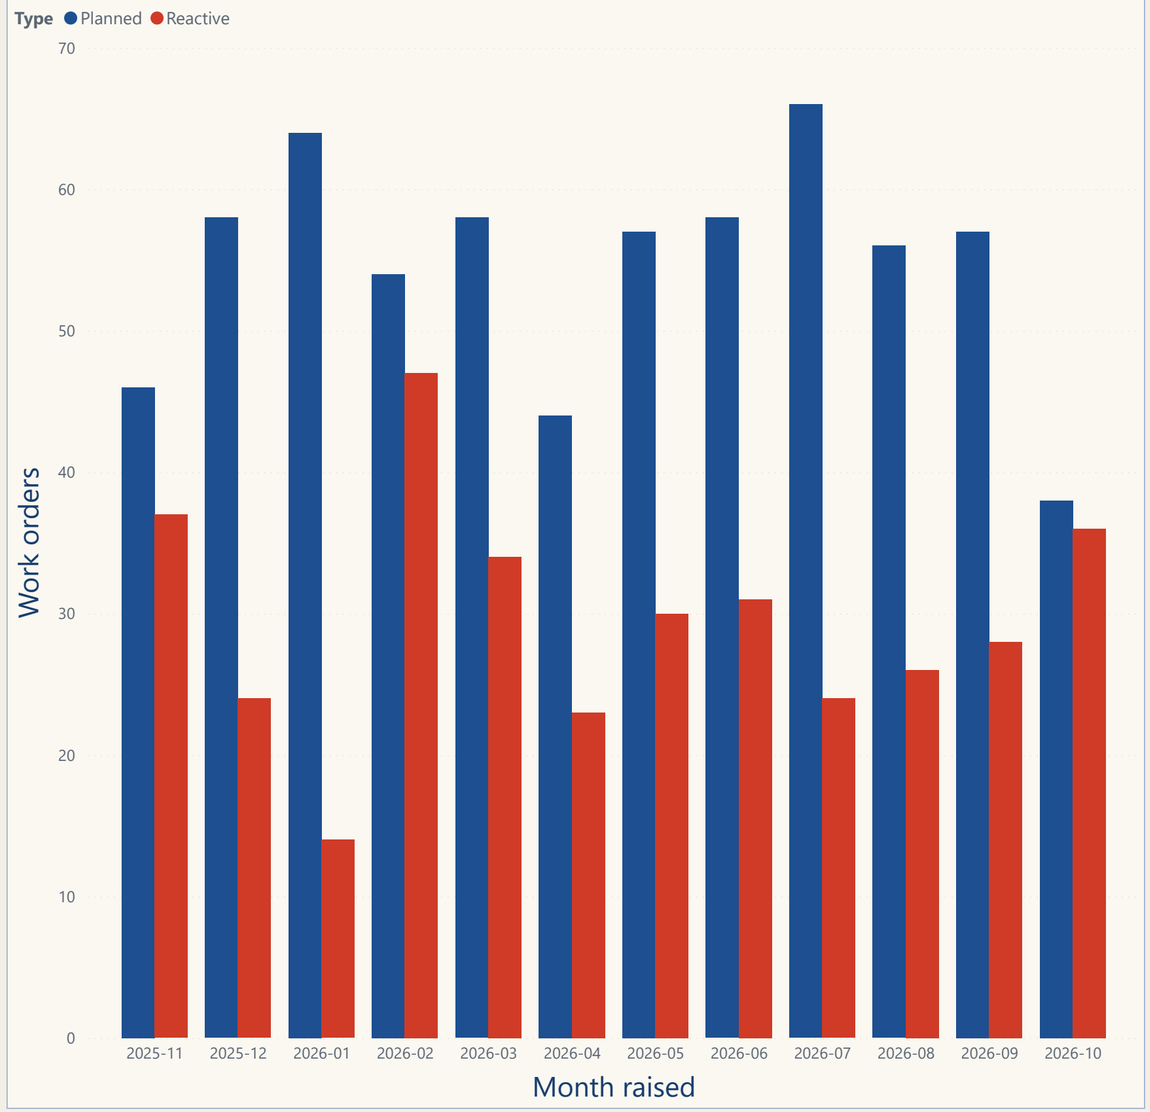

Sample data: these figures are not about TAFE NSW Richmond or any real building (data/sample/README.md says how they were made). Outlines drawn over NSW Imagery and map lots: (c) State of New South Wales (Spatial Services), CC BY 3.0 AU. Suburbs: ABS ASGS 2021 (CC BY 4.0).

IS THE MAINTENANCE BEING DONE?

Planned maintenance done on time each month, essential safety measures by building and status, and the capital works backlog.

Sample data

Planned maintenance on time (Sample data)

88.1%


Safety measures overdue (Sample data)

8


Capital works backlog, AUD (Sample data)

3M

Planned maintenance on time, each month (Sample data)

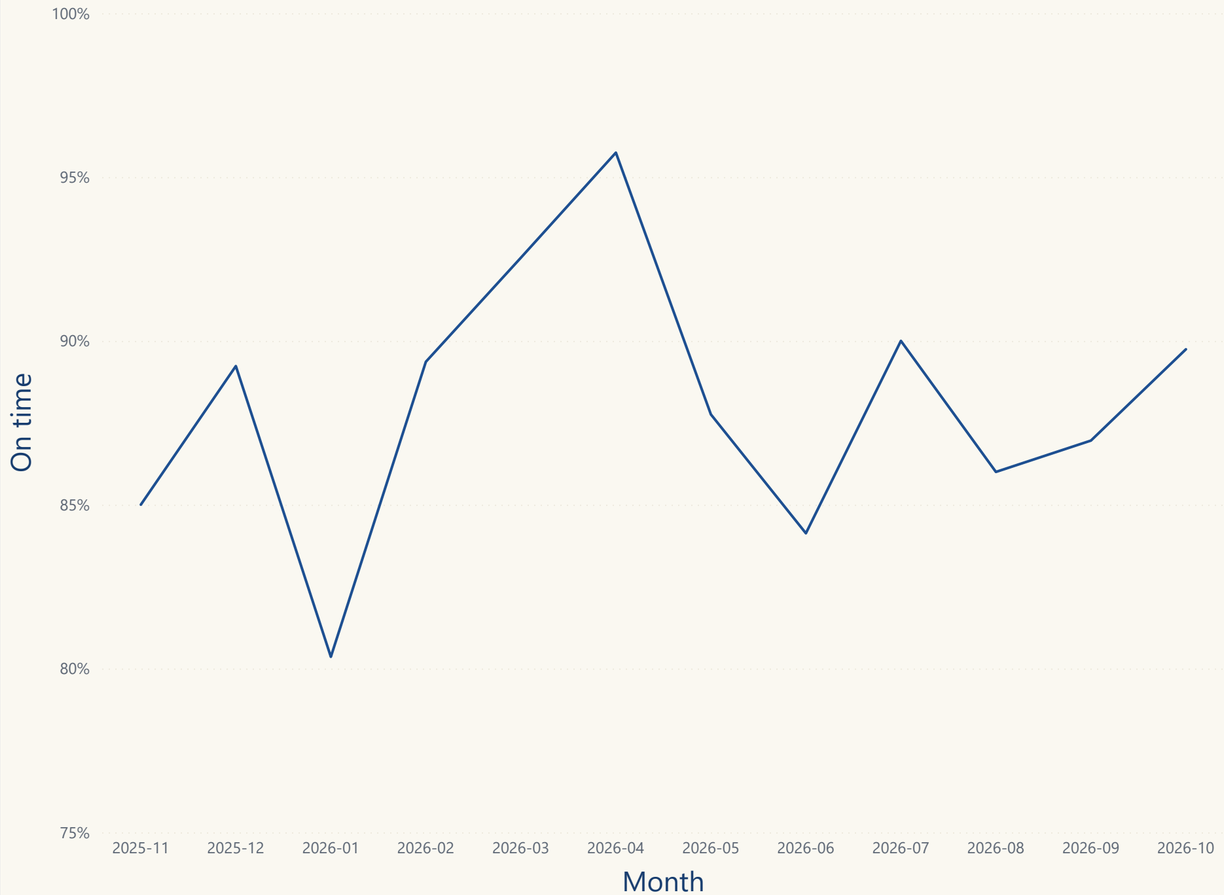

Essential safety measures by building and status (Sample data)

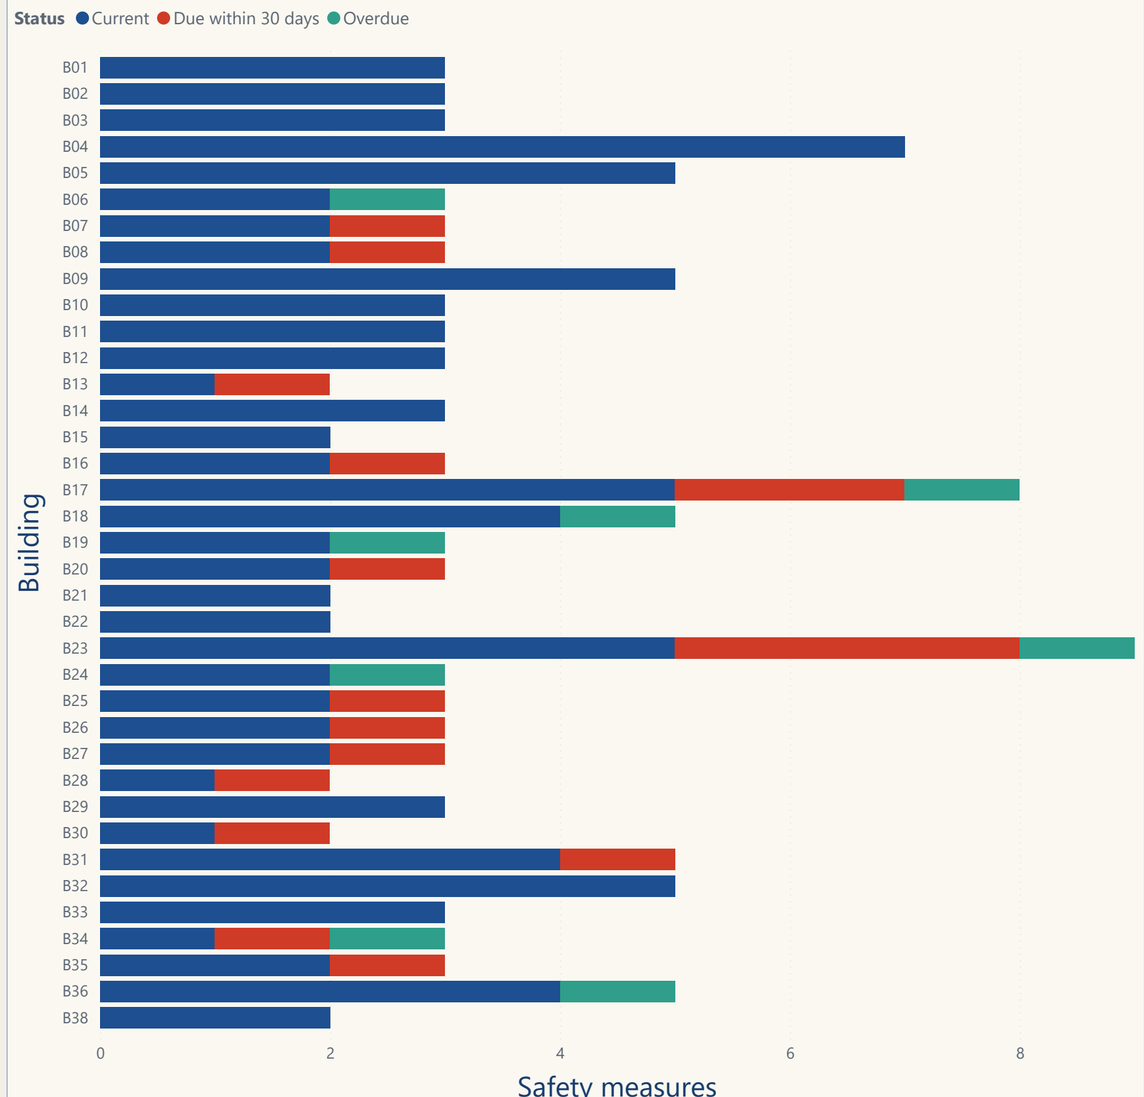

Sample data: these figures are not about TAFE NSW Richmond or any real building (data/sample/README.md says how they were made). Outlines drawn over NSW Imagery and map lots: (c) State of New South Wales (Spatial Services), CC BY 3.0 AU. Suburbs: ABS ASGS 2021 (CC BY 4.0).
